

Effelsberg Status Update


James M Anderson

anderson@mpifr-bonn.mpg.de

Major construction work organized by Klaus Bruns

On behalf of LOFAR

Max-Planck-Institut
für Radioastronomie




LOFAR



MAX-PLANCK-GESELLSCHAFT



Earlier

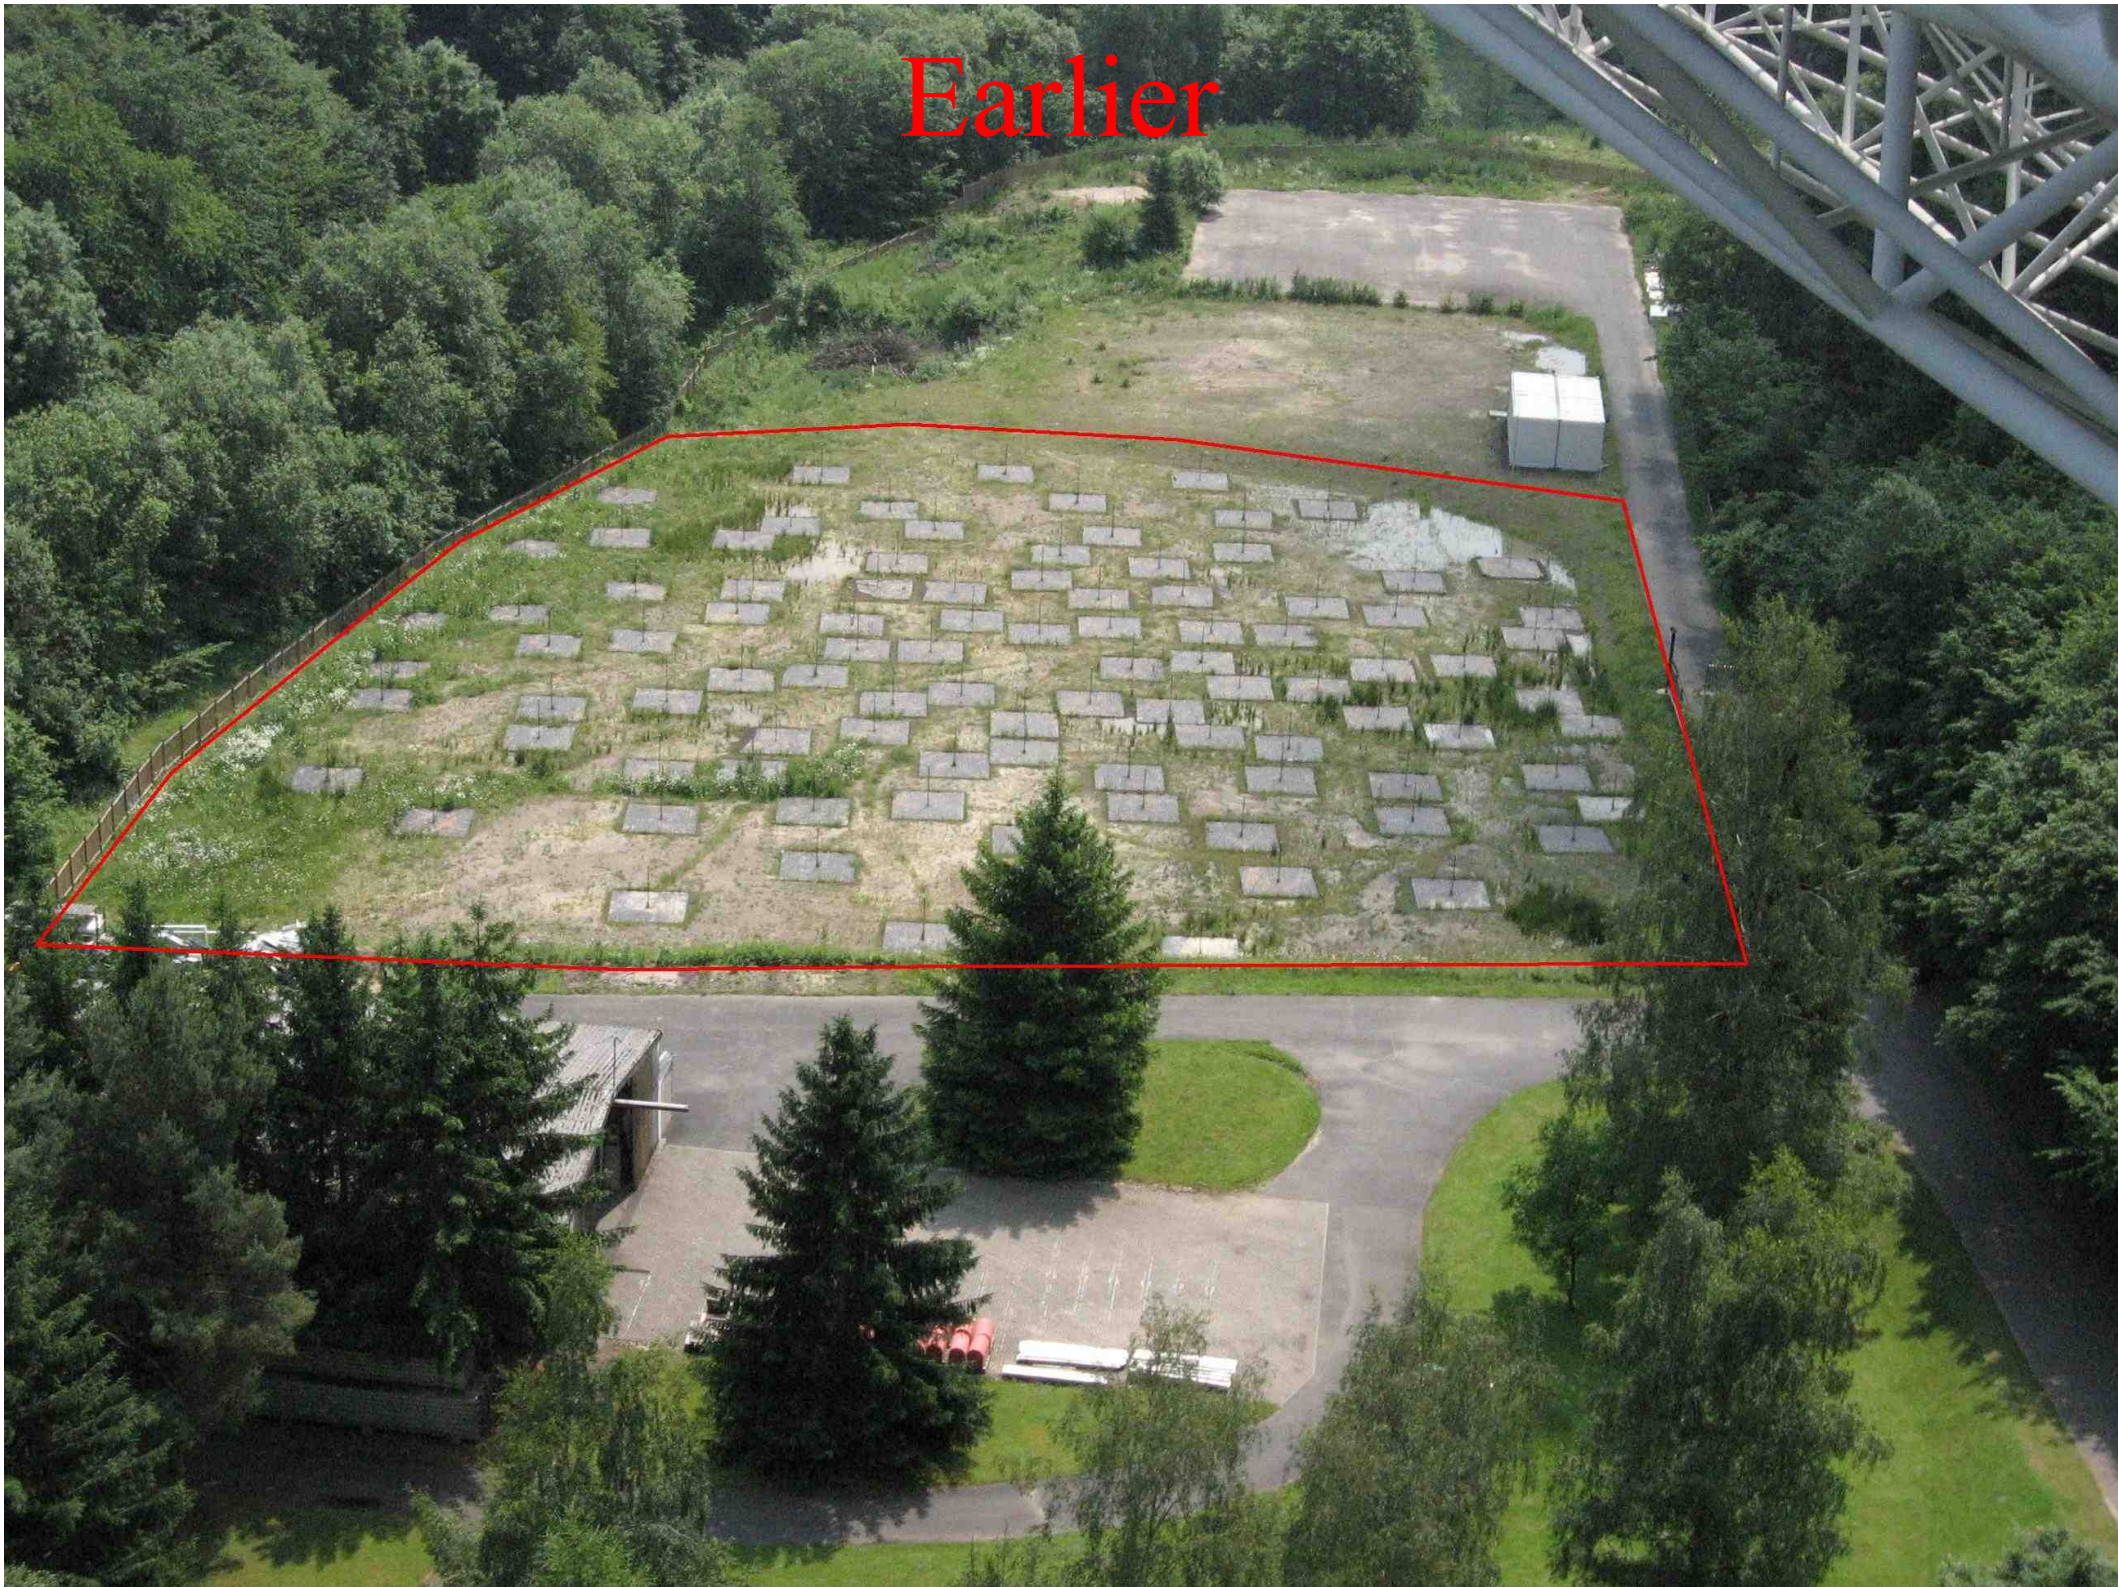

No LBA Dipoles Lost So Far This Year...



Helicopter Pad



Last Week



Reference Marker Measurements (Monday)




Rough Flattening Done



Geopolitical Constraints



Cable Entrance

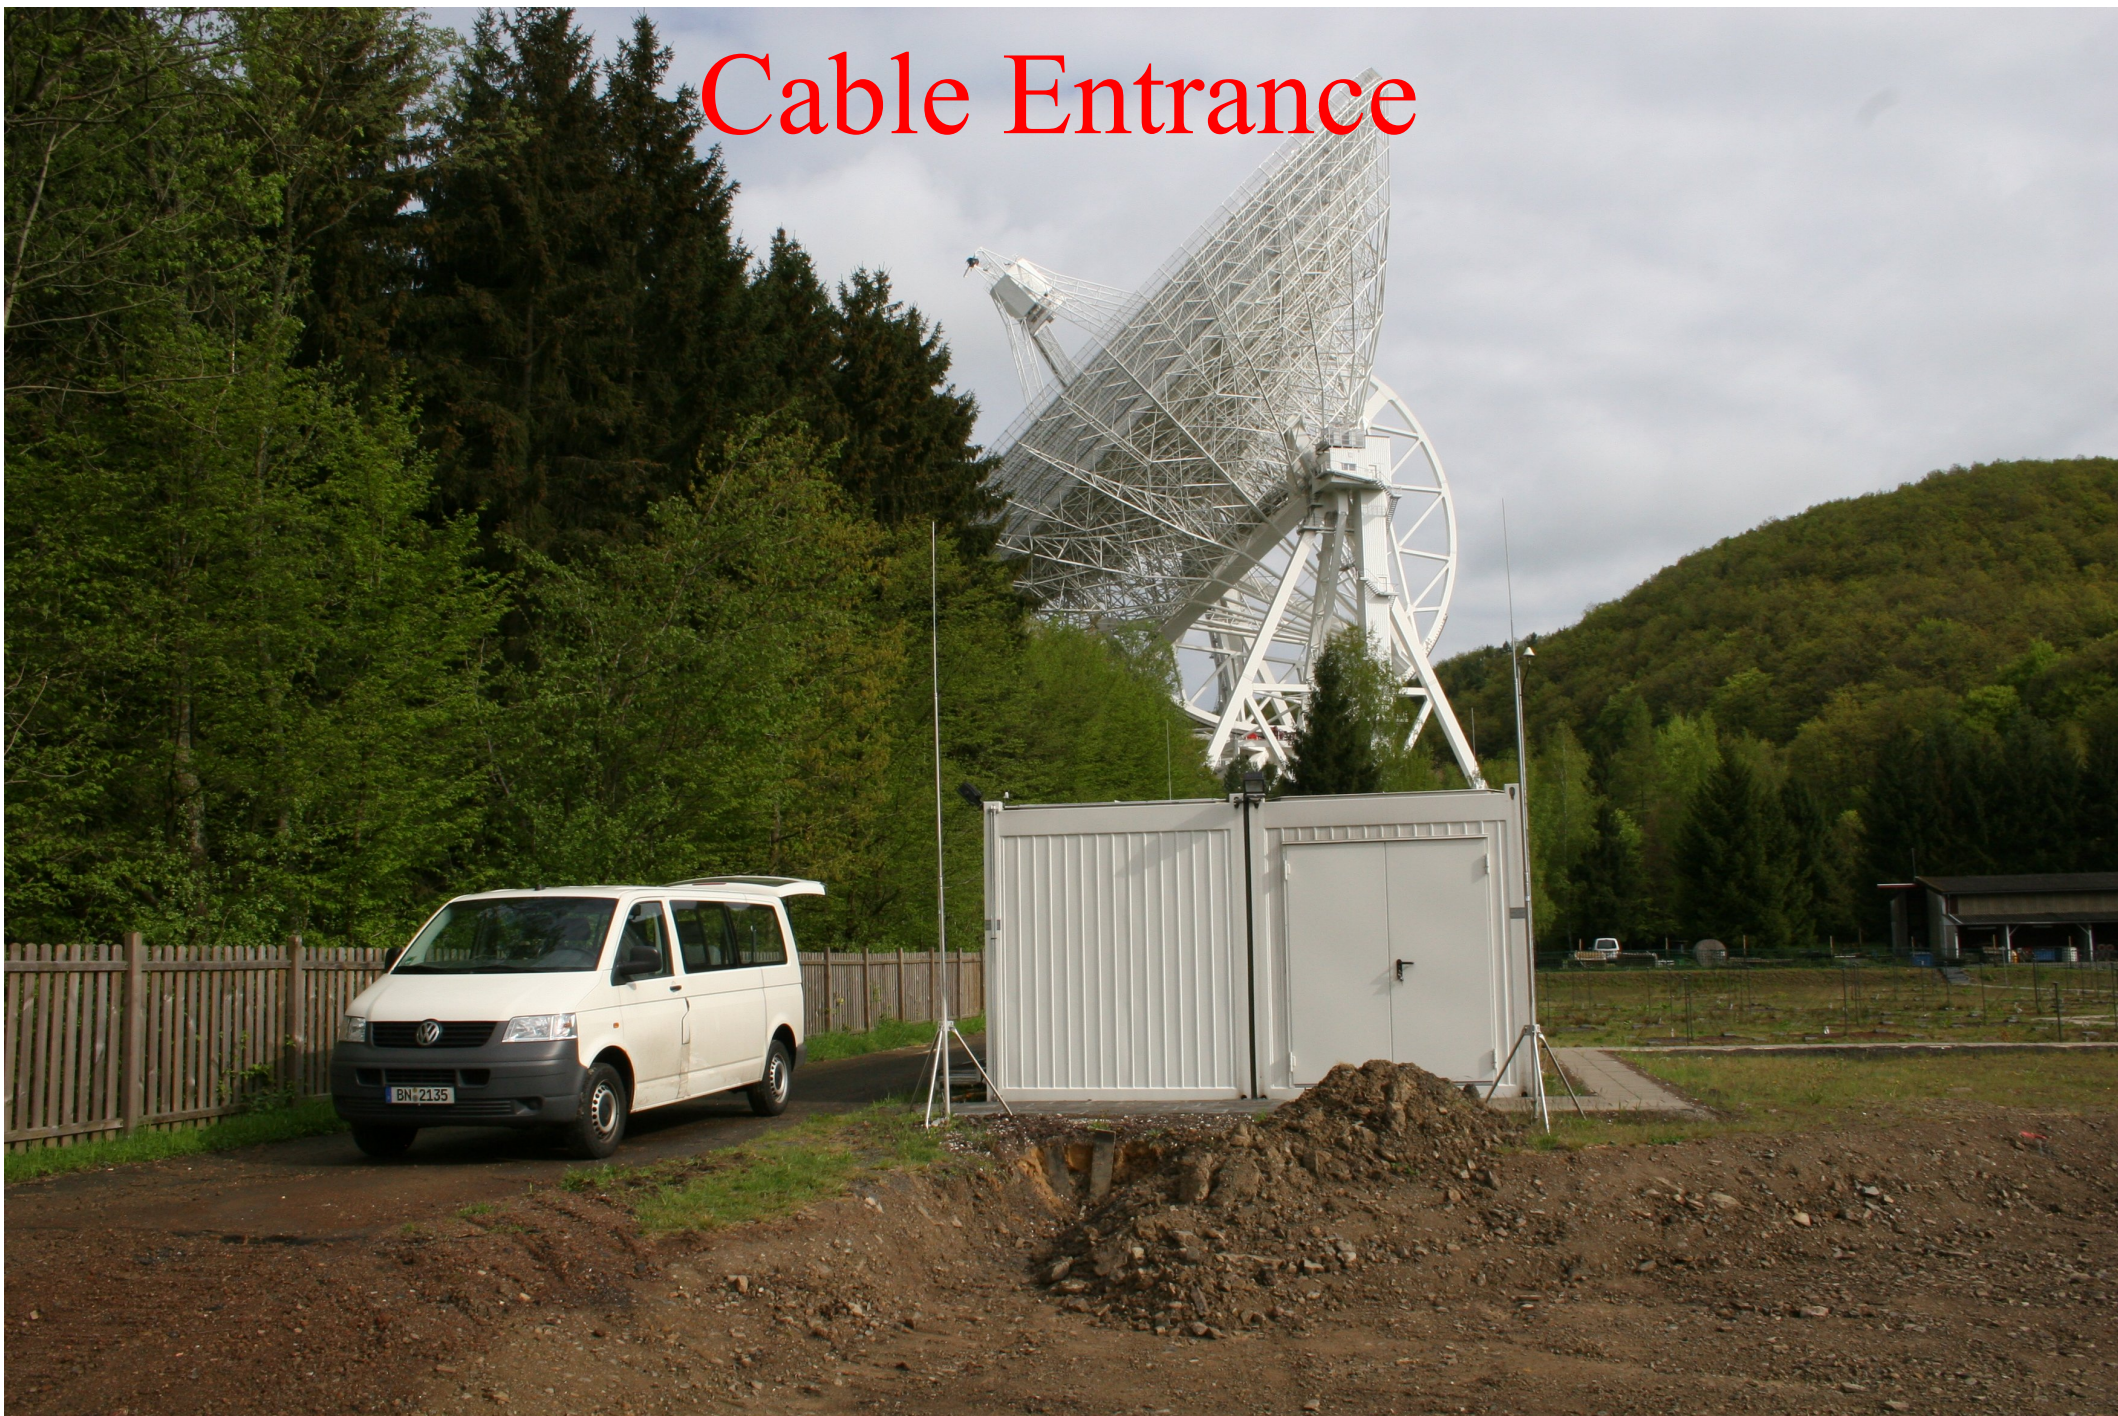

Wildlife



Other Items

- HBA contract not yet signed
 - Negotiations on acceptance tests
- Schedule
 - Cables delivered in week 21?
 - Tile installation hopefully during weeks of June 28 and July 6
- Network
 - Ping test from Bonn to Groningen successful
 - New switch for Effelsberg LOFAR station from ASTRON arrived last week in Bonn
